



BOND 2016

Monthly Project Status

November 2018

1) COMPLETED PROJECTS

1. **New Administration Building** – 1 yr. warranty punch walkthrough completed
2. **High School Softball Batting Cages** – 1 yr. warranty punch walkthrough completed
3. **Tennis Court Improvements** – 1 yr. warranty punch walkthrough completed
4. **Champion HS Football Field Turf** – 1 yr. warranty punch walkthrough completed
5. **Walk-in Freezer/Coolers & Kitchen Improvements** – 1 yr. warranty punch walkthrough completed
6. **District-Wide Roofing** – 1 yr. warranty walkthrough completed
7. **HVAC Upgrades & Repairs** (Curington ES & Cibolo Creek ES) – 1 yr. warranty punch walkthrough completed
8. **Curington and Cibolo Creek Elementary Playgrounds** – 1 yr. warranty punch walkthrough completed
9. **Van Raub ES** – Substantially Complete.
10. **Champion HS Additions & Renovations** – Substantially Complete.
11. **Boerne HS Additions & Renovations** – Substantially Complete.
12. **Boerne MS North Additions & Renovations** – Substantially Complete.
13. **Boerne MS South Additions & Renovations** – Substantially Complete.
14. **HVAC & Controls Upgrades**
 - a. **Pkg. 1** (Kendall ES) – Substantially Complete.
 - b. **Pkg. 2** (Boerne MS South) – Phase 1 Substantially Complete.
15. **Site Improvements**
 - a. **Pkg. 1** (Kendall ES & Boerne MS South) – Substantially Complete.
 - b. **Pkg. 2** (Fair Oaks Ranch ES) – Substantially Complete. **Detention Pond in progress.**
16. **FORES and Kendall ES Playgrounds** – Substantially Complete

2) CONSTRUCTION / DESIGN IN PROGRESS




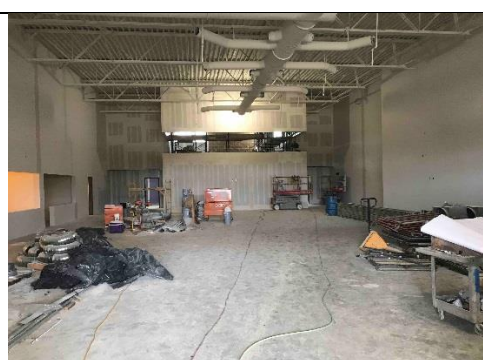
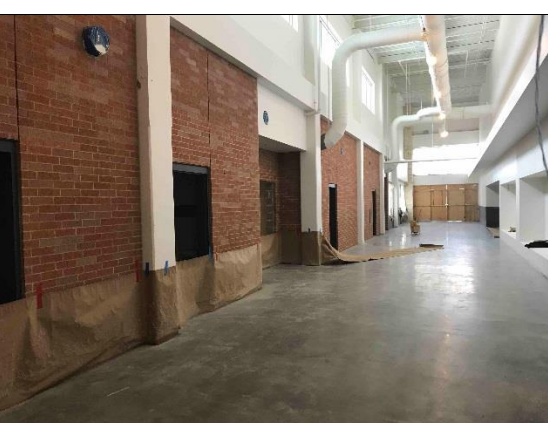

1. **Herff ES** – Retaining walls and sidewalks are being installed. Structural Steel and Metal deck installation, masonry, interior wall framing, gypsum board and mechanical, electrical and plumbing are in progress. Substantial Completion is scheduled for summer 2019.
2. **Voss Middle School** – Brick and Stone installation continues. Building in completely dried-in. Gypsum Board installation, Tape & Float and Ceramic Tile installation are in progress. Mechanical, Plumbing & Electrical are in progress. Installation of water line to the site and Hwy 46 access are in progress. Substantial Completion is scheduled for summer 2019.
3. **BHS Softball Field Backstop Netting** – Construction in progress. Structural Shop Drawings being generated.
4. **BHS, CHS & BMSS Security Vestibules** – In design phase.

3) SUMMER 2019 PROJECTS (in progress)

1. **Boerne MS South** (HVAC & Controls Upgrades) – Phase 2 HVAC
2. **Boerne MS South Cafeteria** – Ceiling Acoustical Treatment
3. **BHS, CHS & BMSS Security Vestibules** – Summer 2019 construction

BOND 2016
Monthly Project Status
 November 2018

4) VOSS MIDDLE SCHOOL

	
<p>Site development – sidewalks, concrete curbs</p>	<p>Main Entrance Security Vestibule</p>
	
<p>Gymnasium Entrance</p>	<p>Library interior work in progress</p>
	
<p>Gymnasium corridor with polished concrete floor</p>	<p>Restroom plumbing fixture installation</p>



BOND 2016
Monthly Project Status
 November 2018

5) HERFF ELEMENTARY SCHOOL



	
<p>Courtyard View to two story classrooms. Exterior wall sheathing and masonry columns</p>	<p>Courtyard View to the Gymnasium. Exterior wall sheathing and masonry columns</p>
	
<p>Installation of interior stairs and ramp are in progress.</p>	<p>Stud wall framing at 2nd floor. Interior concrete ramp and stairs.</p>
	
<p>Cafeteria Dining Room interior work in progress.</p>	<p>Moisture resistant gypsum board is being installed at areas that are already weathered-in.</p>

BOND 2016
Monthly Project Status
 November 2018

6) BOERNE MS NORTH FINE ARTS


	
<p>Band Hall Music Filing Cabinets</p>	<p>Choir Room - Wenger Acoustical Practice Room, Markerboard w/music lines and Projection Screen</p>

7) BOERNE HIGH SCHOOL – SECURITY VESTIBULE

	
<p>Existing Conditions</p>	<p>Proposed Improvements</p>

BOND 2016
Monthly Project Status
 November 2018

8) CHAMPION HS – SECURITY VESTIBULE

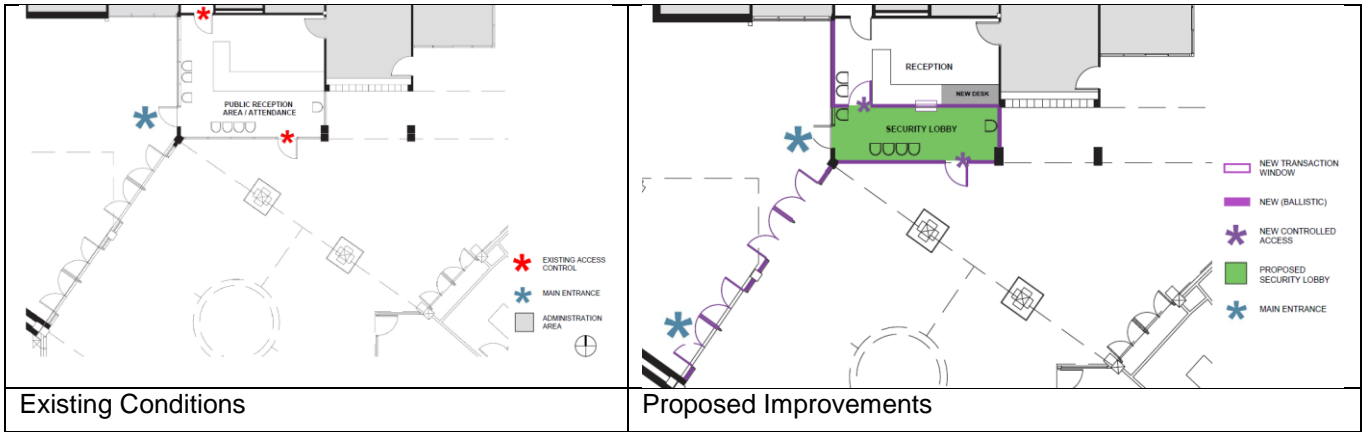

9) BOERNE MS SOUTH – SECURITY VESTIBULE

